

A	B	C	D	E	F	G	H	I	J	K	L
	BUDGETED				ACTUAL				PRODUCTIVITY PROJECTED		
Activity	Units	UOM	Hours		Units	UOM	% Comp.	Earned Hrs.	Act. Hours	Earned/Actual	Hours
A	1000	LF	800		300	LF	30.00%	240	275	87.27%	917.00
B	5000	SQ FT	1500		2500	SQ FT	50.00%	750	675	111.11%	1350.00
C	500	EA	550		100	EA	20.00%	110	80	137.50%	400.00
D	1	LS	150		80.00%	LS	80.00%	120	120	100.00%	150.00
TOTAL			3000					1220	1150	106.09%	2817.00


Weekly Productivity Report

EXAMPLE User-Friendly Report Formats

Project (Hours)

Cost Code	Budget	Used	Earned
41-00	3,741	2,013	1,890
45-00	2,828	1,112	601
51-00	2,110	232	567
52-00	976	143	0
55-00	667	201	343
62-00	801	1,361	801
181-00	1,950	988	1,132
300-00	320	56	70
301-00	960	453	131
Total Job:	14,353	6,559	5,535

Job Name: Beantown Marketplace
Week Ending: 7/9/2023

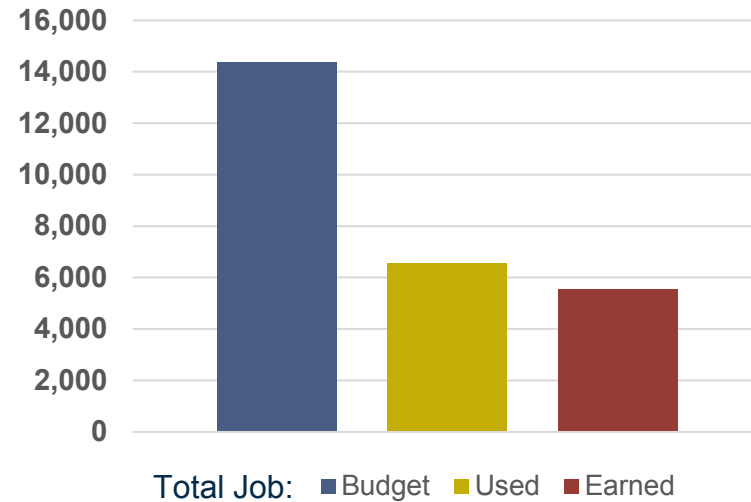

Project (Hours)

